

Name Ayush

SRN PES1UG24AM909

SEC D

Epic:

An agile epic is a body of work that can be broken down into specific tasks (called user stories) based on the needs/requests of customers or end-users.

Epics are an important practice for agile and DevOps teams.

Epic allows us to break down large complex tasks into small easier ones.

Epic1: Table Discovery & Reservation

Enable diners to select an available table from a live 2D floor plan for a chosen date/time.

Epic2: Menu Pre-Ordering

Let diners browse the menu, customize items, and link a pre-order to their reservation.


Epic3: Kitchen Timeline & Prep Management


Automatically compute prep timelines and queue kitchen tickets aligned to arrival time.

Epic4: Floor Management & Status Tracking


Give managers real-time control over table status across all terminals.

Epic Creation

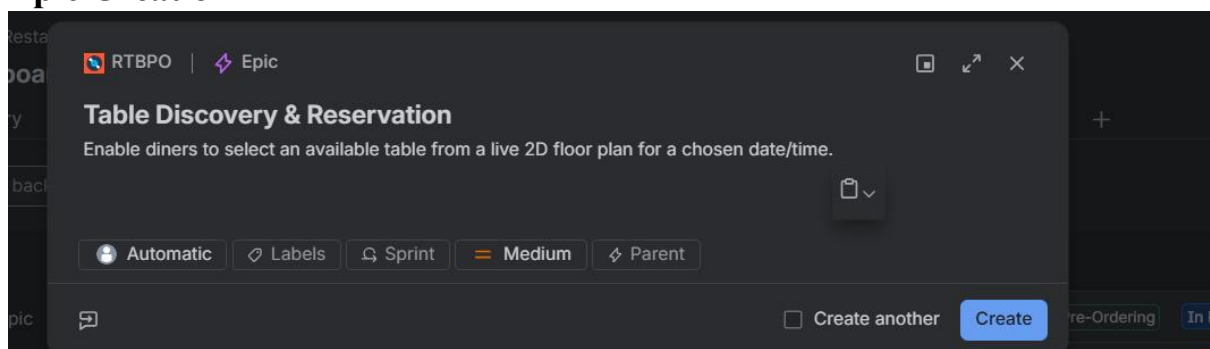

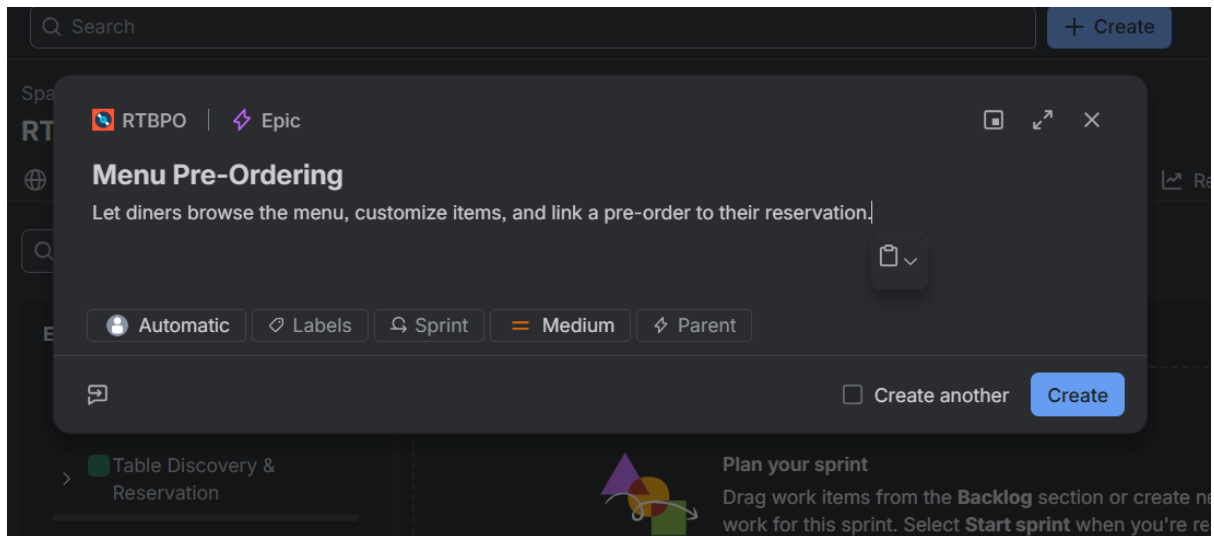

Epic Table

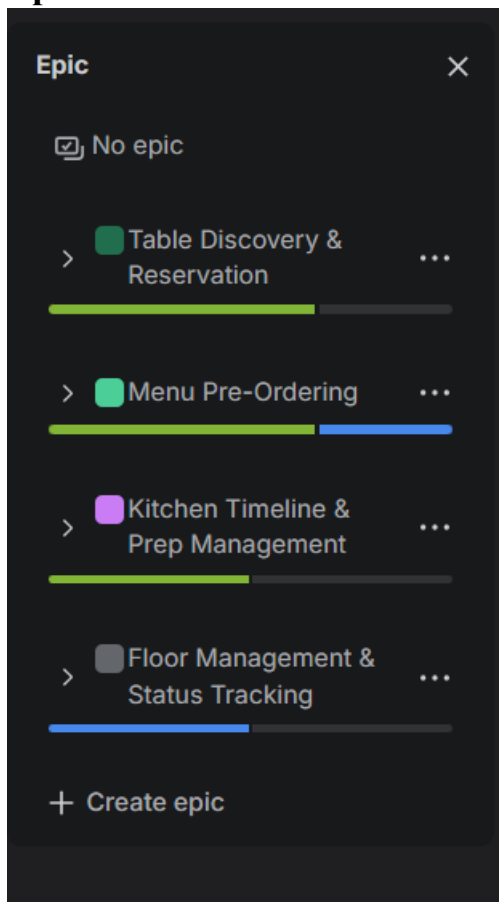

User Stories:

A user story is an informal, general explanation of a software feature written from the perspective of the end user. Its purpose is to articulate how a software feature will provide value to the customer.

It's tempting to think that user stories are, simply put, software system requirements. But they're not.

User story gives us the perspective of the end-user or Customer.

Story1.1: Browse Floor Plan

As a diner, I want to view the interactive 2D floor layout with real-time table availability, so that I can see which tables are open.

Points: 3

Story1.2: Select & Lock Table

As a diner, I want to select an available table for my party size and have it temporarily held, so that I have time to complete my booking without losing the table.

Points: 5

Story1.3 Cancel Reservation

As a diner, I want to cancel a reservation I've made, so that I can free up the table if my plans change.

Points: 2

Story2.1: Browse Digital Menu

As a diner, I want to browse the restaurant's digital menu, so that I can decide what to pre-order.

Points: 2

Story2.2: Customize Order

As a diner, I want to customize items and add dietary notes, so that my food matches my preferences.

Points: 3

Story2.3: Link Order to Reservation

As a diner, I want to attach my pre-order to my table booking, so that my food is ready when I arrive.

Points: 3

Story3.1: Prep Time Calculation

As the system, I want to automatically calculate estimated prep time based on order volume, so that food is timed to be ready, not early or late.

Points:8

Story3.2: Track Kitchen Prep Queue

As a restaurant manager, I want to view the live kitchen prep ticket queue, so that staff can prioritize orders correctly.

Points:5

Story4.1: Manage Floor Plan Status

As a restaurant manager, I want to manually or automatically update table status, so that the floor plan always reflects reality.



Points:5

Story4.2: Real-Time Status Sync

As a restaurant manager, I want to see status changes sync across all terminals in under 500ms, so that I never act on stale table data.

Points:8

Story Creation:

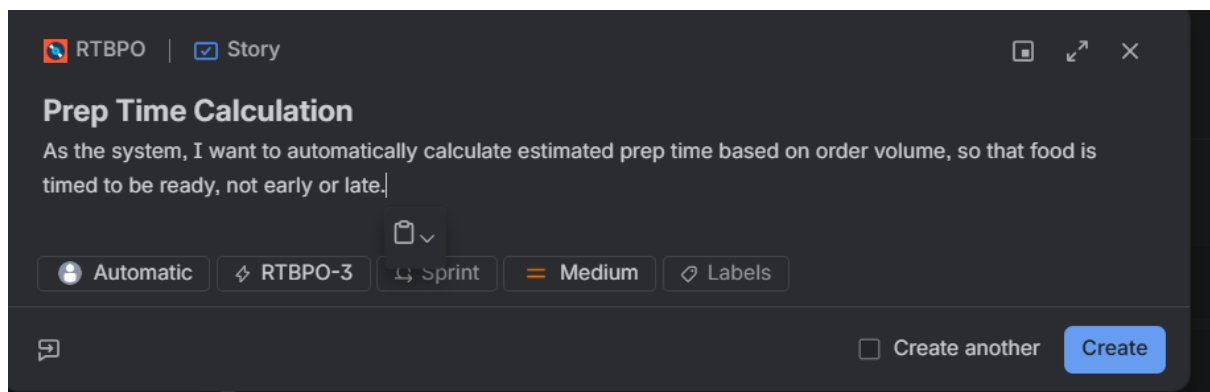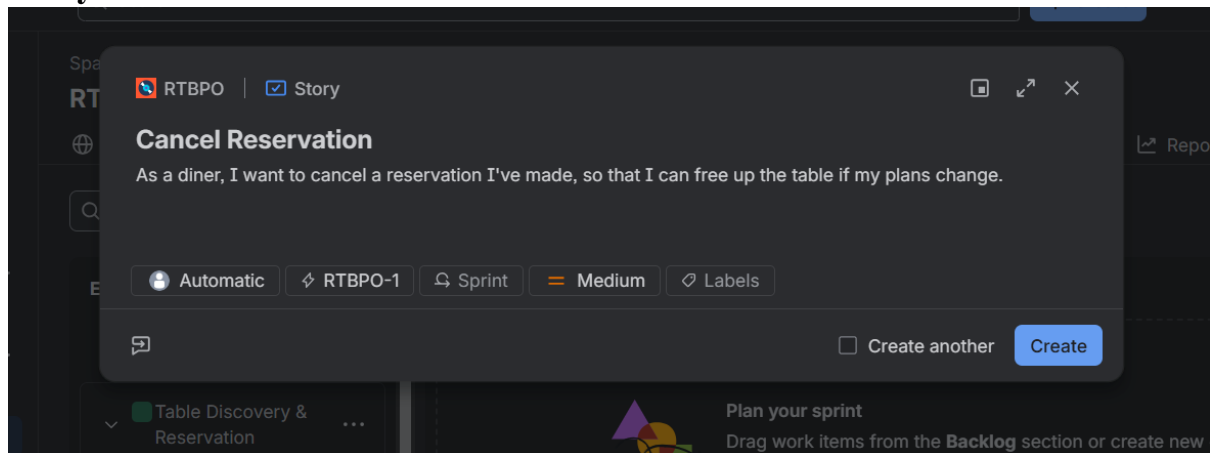

Stories in Sprint1(with Points)

RTBPO Sprint 1 31 Aug - 7 Sep (7 work items)									
*Deliver core table reservation and pre-order flow									
☒	RTBPO-5	Browse Floor Plan	Table Dis...	To Do ▾	3	=			
☒	RTBPO-6	Select & Lock Table	Table Dis...	To Do ▾	5	=			
☒	RTBPO-9	Browse Digital Menu	Menu Pre...	To Do ▾	2	=			
☒	RTBPO-10	Link Order to Reservation	Menu Pre...	To Do ▾	3	=			
☒	RTBPO-11	Customize Order	Menu Pre...	To Do ▾	3	=			
☒	RTBPO-12	Prep Time Calculation	Kitchen Ti...	To Do ▾	8	=			
☐	☒	RTBPO-14	Manage Floor Plan Status	Floor Man...	To Do ▾	5	=		...

Reordered Stories

RTBPO Sprint 2 7 Sep – 14 Sep (5 work items)				22	0	0	Start sprint	...
☒	RTBPO-15	Real-Time Status Sync		To Do ▾	8			
☒	RTBPO-14	Manage Floor Plan Status		To Do ▾	5			
☐	☒	RTBPO-9 Browse Digital Menu		To Do ▾	2			...
☐	☒	RTBPO-13 Track Kitchen Prep Queue		To Do ▾	5			...
☒	RTBPO-7	Cancel Reservation		To Do ▾	2			

Creation of Sprint:

Search

/ Restaurant

PO board

Summary

Search backlog

☒ Kitchen
Prep Ma

☐ Floor Ma
Status Tr

Work items
Completed

mate

of estimated w

Work item unesti

View

Create work item

Edit sprint: RTBPO Sprint 1

Required fields are marked with an asterisk *

Sprint name *

RTBPO Sprint 1

Duration

1 week

Start date

8/31/2026 9:00 AM

Date format: MM/DD/YYYY. Time format: e.g. 1:00 PM.

End date


9/7/2026 9:00 AM

Sprint goal


'Deliver core table reservation and pre-order flow'

Cancel Update

Before start of the Sprint:

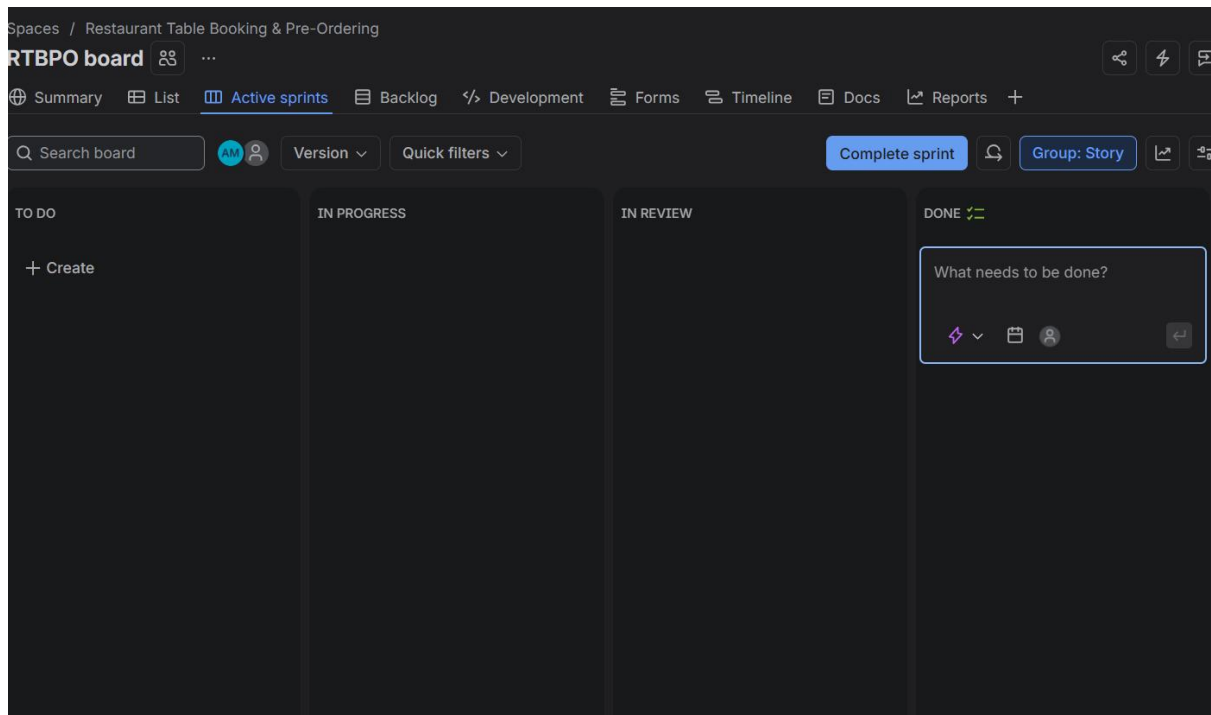

Active Sprint1:

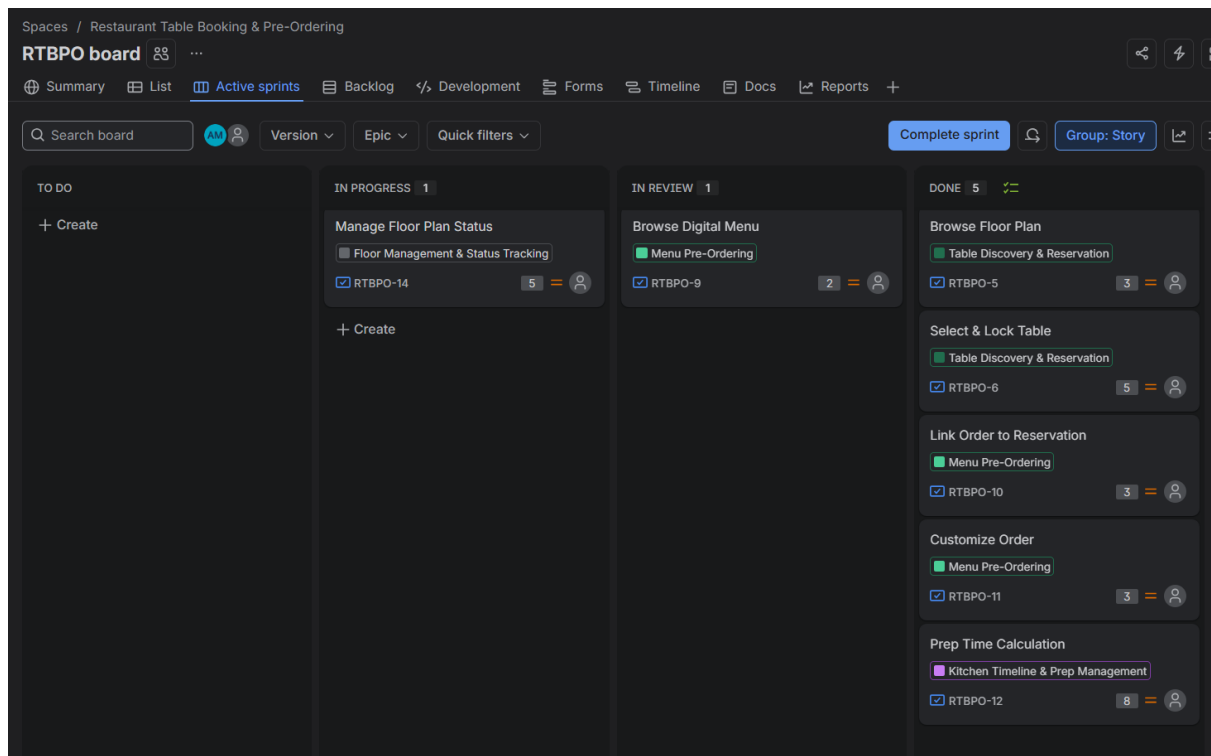

Active Sprint2:

Summary

List

Active sprints

Backlog

Development

Forms

Timeline

Docs

Reports

Search board

AM

Version

Epic

Quick filters

Complete sprint

Group: Story

TO DO

What needs to be done?

IN PROGRESS 1

Browse Digital Menu

Menu Pre-Ordering

RTBPO-9

2

IN REVIEW 1

Real-Time Status Sync

Floor Management & Status Tracking

RTBPO-15

8

DONE 3

Manage Floor Plan Status

Floor Management & Status Tracking

RTBPO-14

5

Track Kitchen Prep Queue

Kitchen Timeline & Prep Management

RTBPO-13

5

Cancel Reservation

Table Discovery & Reservation

RTBPO-7

2

+ Create

Comments on Epic:



Ayush M [🔗](#)

1 second ago

"All 3 stories (Browse Floor Plan, Select & Lock Table, Cancel Reservation) covered across Sprint 1 and Sprint 2. Core table locking and reservation flow is functional; overbooking prevention logic aligns with FR-001 acceptance criteria."



Ayush M [🔗](#)


now

"Browse Digital Menu and Customize Order completed in Sprint 1; Link Order to Reservation tested end-to-end with the table booking flow. Pre-order data now successfully attaches to the reservation ID as required by FR-002."




Burndown Chart:

After Sprint1:

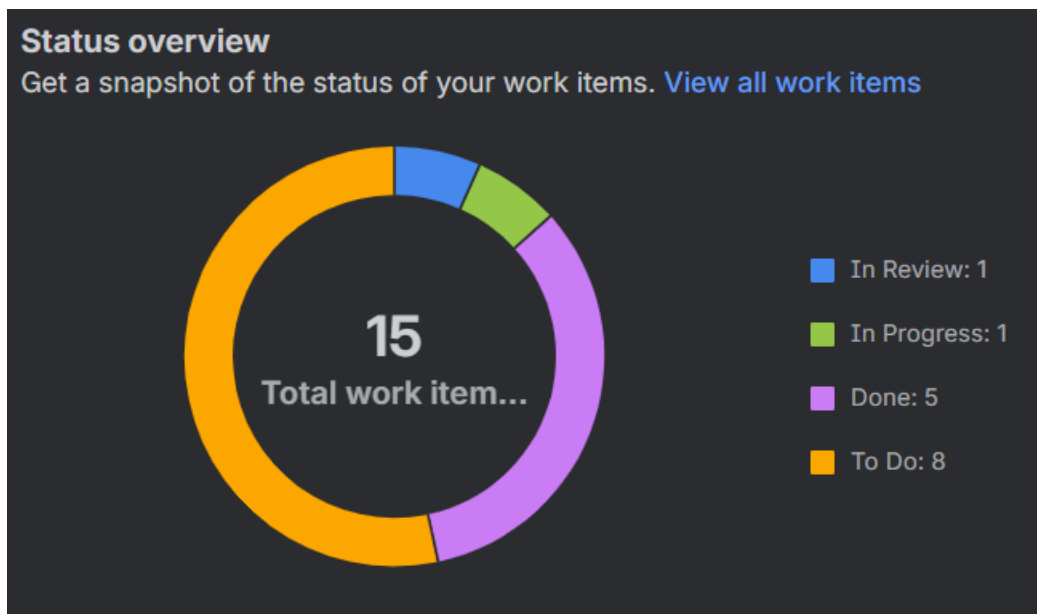


After Sprint2:

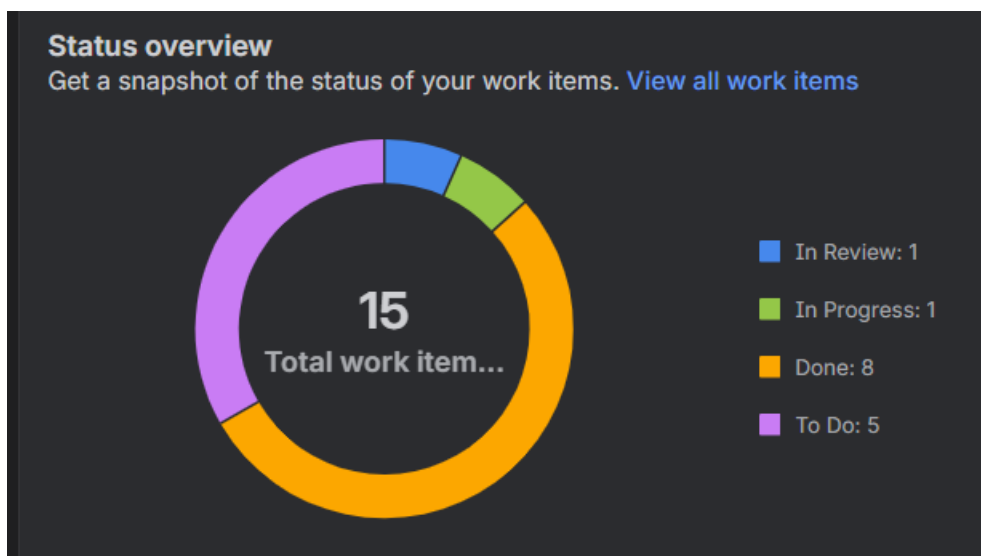

Work item creation trend

In Progress Done In Review To Do

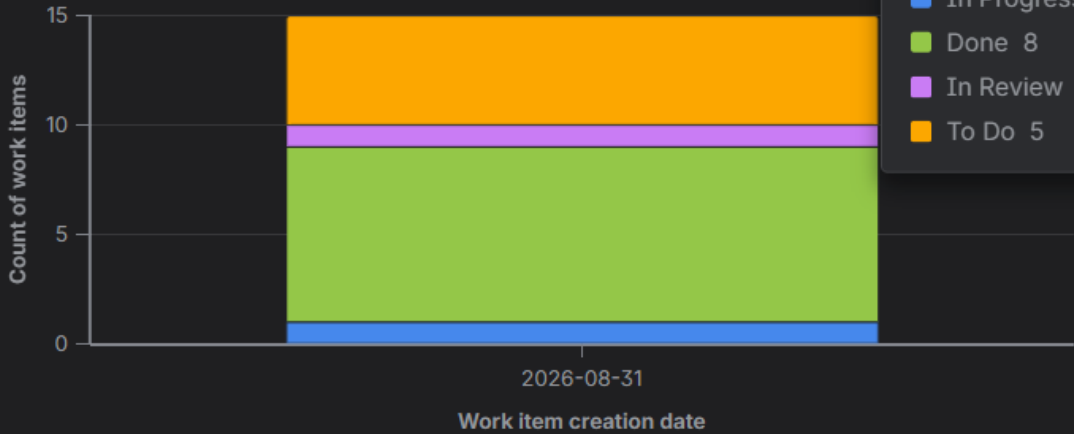

Planning Poker Introduction (Reflection):

For this lab, Planning Poker was simulated individually rather than with a live team, but the same estimation logic was applied to each user story before it was added to a sprint. For every story, the following questions were considered before assigning a Fibonacci point value: how many system components does this touch (UI, backend, kitchen sync, payment gateway, etc.), how much uncertainty exists in the implementation, and how it compares in complexity to a story that was already estimated.

For example, "**Browse Floor Plan**" was estimated at **3 points** — a straightforward read-only UI feature with low uncertainty. In contrast, "**Prep Time Calculation**" was estimated at **8 points**, since it involves a non-trivial algorithm (order volume → prep time → backward scheduling from arrival time) with more edge cases and higher implementation risk. Similarly, "**Real-Time Status Sync**" was rated **8 points** due to the added complexity of maintaining sub-500ms latency across concurrent manager terminals — a much harder problem than a simple CRUD-style story like "**Cancel Reservation**" (2 points).

This comparative, relative-sizing approach — anchoring new estimates against previously-estimated stories rather than guessing in a vacuum — is the core value Planning Poker provides, even outside a live group setting.

This comparative, relative-sizing approach — anchoring new estimates against previously-estimated stories rather than guessing in a vacuum — is the core value Planning Poker provides, even outside a live group setting.

Group Reflection

Sprint 1 (7 stories, 29 points) focused on the core diner journey: browsing the floor plan, locking a table, customizing and linking a food order, calculating prep time, and updating floor status. By the end of Sprint 1, **5 of 7 stories were fully Done**, with 1 in Progress and 1 in Review — a completion rate of roughly 71%, close to the sprint's planned velocity.

Sprint 2 (5 stories, 15 points) carried forward the two unfinished items from Sprint 1 and added three new stories: Cancel Reservation, Track Kitchen Prep Queue, and Real-Time Status Sync. By the end of Sprint 2, cumulative Done items rose from 5 to **8**, with 1 story still In Progress (Browse Digital Menu) and 1 in Review (Real-Time Status Sync).

What went well: Prioritizing high-value, high-priority stories (Manage Floor Plan Status, Real-Time Status Sync) early in the backlog kept the team focused on features that unblock the core booking flow first.

What could improve: A couple of stories (Browse Digital Menu, Real-Time Status Sync) spilled across sprint boundaries rather than reaching Done within their original sprint — suggesting either the estimates were slightly optimistic, or these stories should have been broken into smaller sub-tasks (e.g. separating "sync logic" from "UI status indicators") to finish cleanly within a single sprint.

Takeaway: The burndown and status-overview data across both sprints show steady, incremental progress consistent with Agile's iterative delivery model — each sprint reduced the backlog while surfacing realistic friction points (spillover, estimation accuracy) that a real team would address in a sprint retrospective.

